Phase 1 Schedule
(current scope of work)

Deschutes County Landfill Siting Study - Develop Short List of Sites

ID	Task Name	Duration	Start	Finish
1	Finalize Criteria	45 days	Mon 12/6/21	Fri 2/4/22
2	Refine Site Selection Process	155 days	Mon 12/6/21	Fri 7/8/22
3	Implement Site Selection Process	175 days	Mon 4/4/22	Fri 12/2/22
4	Facilitate Site Selection Process	330 days	Mon 12/6/21	Fri 3/31/23
5	Provide Public Outreach	157 days	Mon 1/31/22	Fri 3/31/23
6	Provide State and Local Entitlements Summary	155 days	Mon 12/6/21	Fri 3/31/23
7	Document Process	158 days	Mon 1/3/22	Fri 3/31/23
8	Project Management	330 days	Mon 12/6/21	Fri 3/31/23

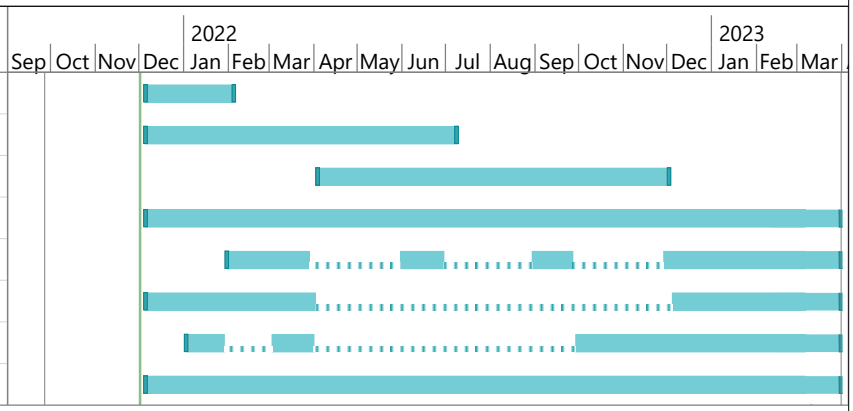

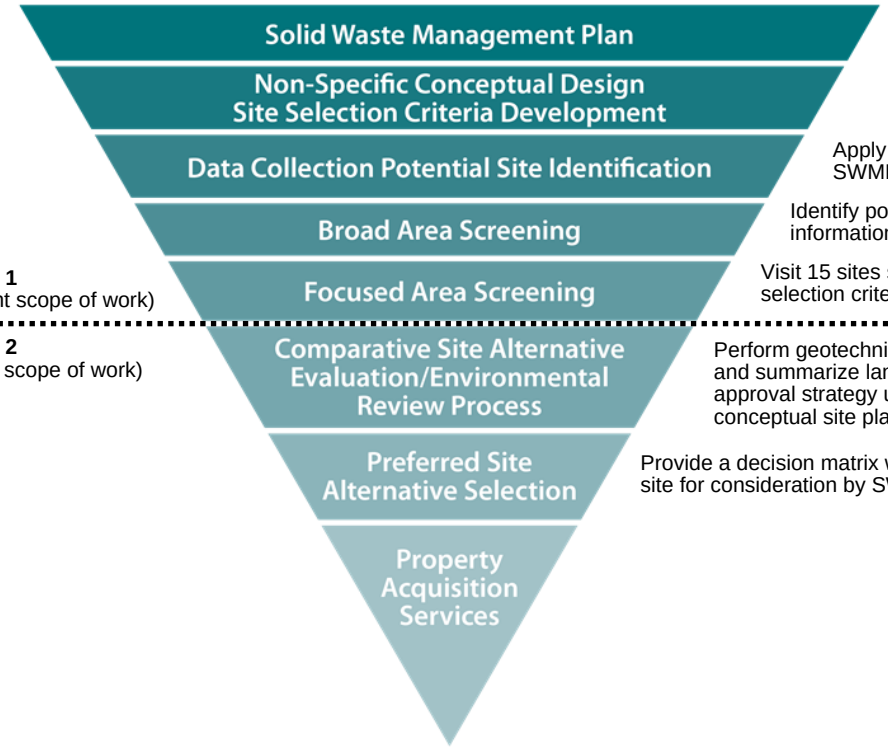

Apply fatal flaw criteria via GIS data to identify potential areas where SWMF facility can be developed

Identify potential sites and evaluate against the site selection criteria, based on available GIS and online information. Select 15 top-scoring sites to proceed to Focused Area Screening.

Phase 1
(current scope of work)

Visit 15 sites selected and gather additional information with non-invasive studies. Evaluate against the site selection criteria, based on field studies, to select 3-5 top-scoring sites for Comparitive Site Alternative Evaluation.

Phase 2
(future scope of work)

Perform geotechnical, environmental, and cultural resources studies on the 3-5 sites. Confirm and summarize land use and entitlements process required for each site. Prepare permit approval strategy under environmental, land use, and solid waste regulations. Prepare conceptual site plans and preliminary cost estimates for comparison of each potential site.

Provide a decision matrix with weighted criteria and recommended SWMF site for consideration by SWAC and Board of County Commissioners.
